Projected Project Stats During Demo & Excavation

Demo: 8 Week Duration
- 4 trucks total; 2 in alley, 1 at landfill, and 1 in route
- Landfill located on 93
- Recycle located at I-76 & 72nd

Shoring: 6 Week Duration
- Mobilization = 5 Semi Trucks
- 1 concrete truck/20 min for 2 hrs at the end of the day
- Spoil removal = Approx. 30 trucks / week or as necessary

Excavation: 9-10 Week Duration
- 800 Yd/Day (avg.) = 12 trucks/hr = 95-100 trucks/day

Noise and Work Hour Ordinances
- Work Hours: 7:00 AM - 6:00 PM (with variance)
- Trucking Hours: 7:00 AM - 4:00 PM (stop time for staging on Broadway)
- Noise Ordinance: 80 dBA at property line. JE Dunn will submit a request for variance based on the anticipated noise during the demolition phase.
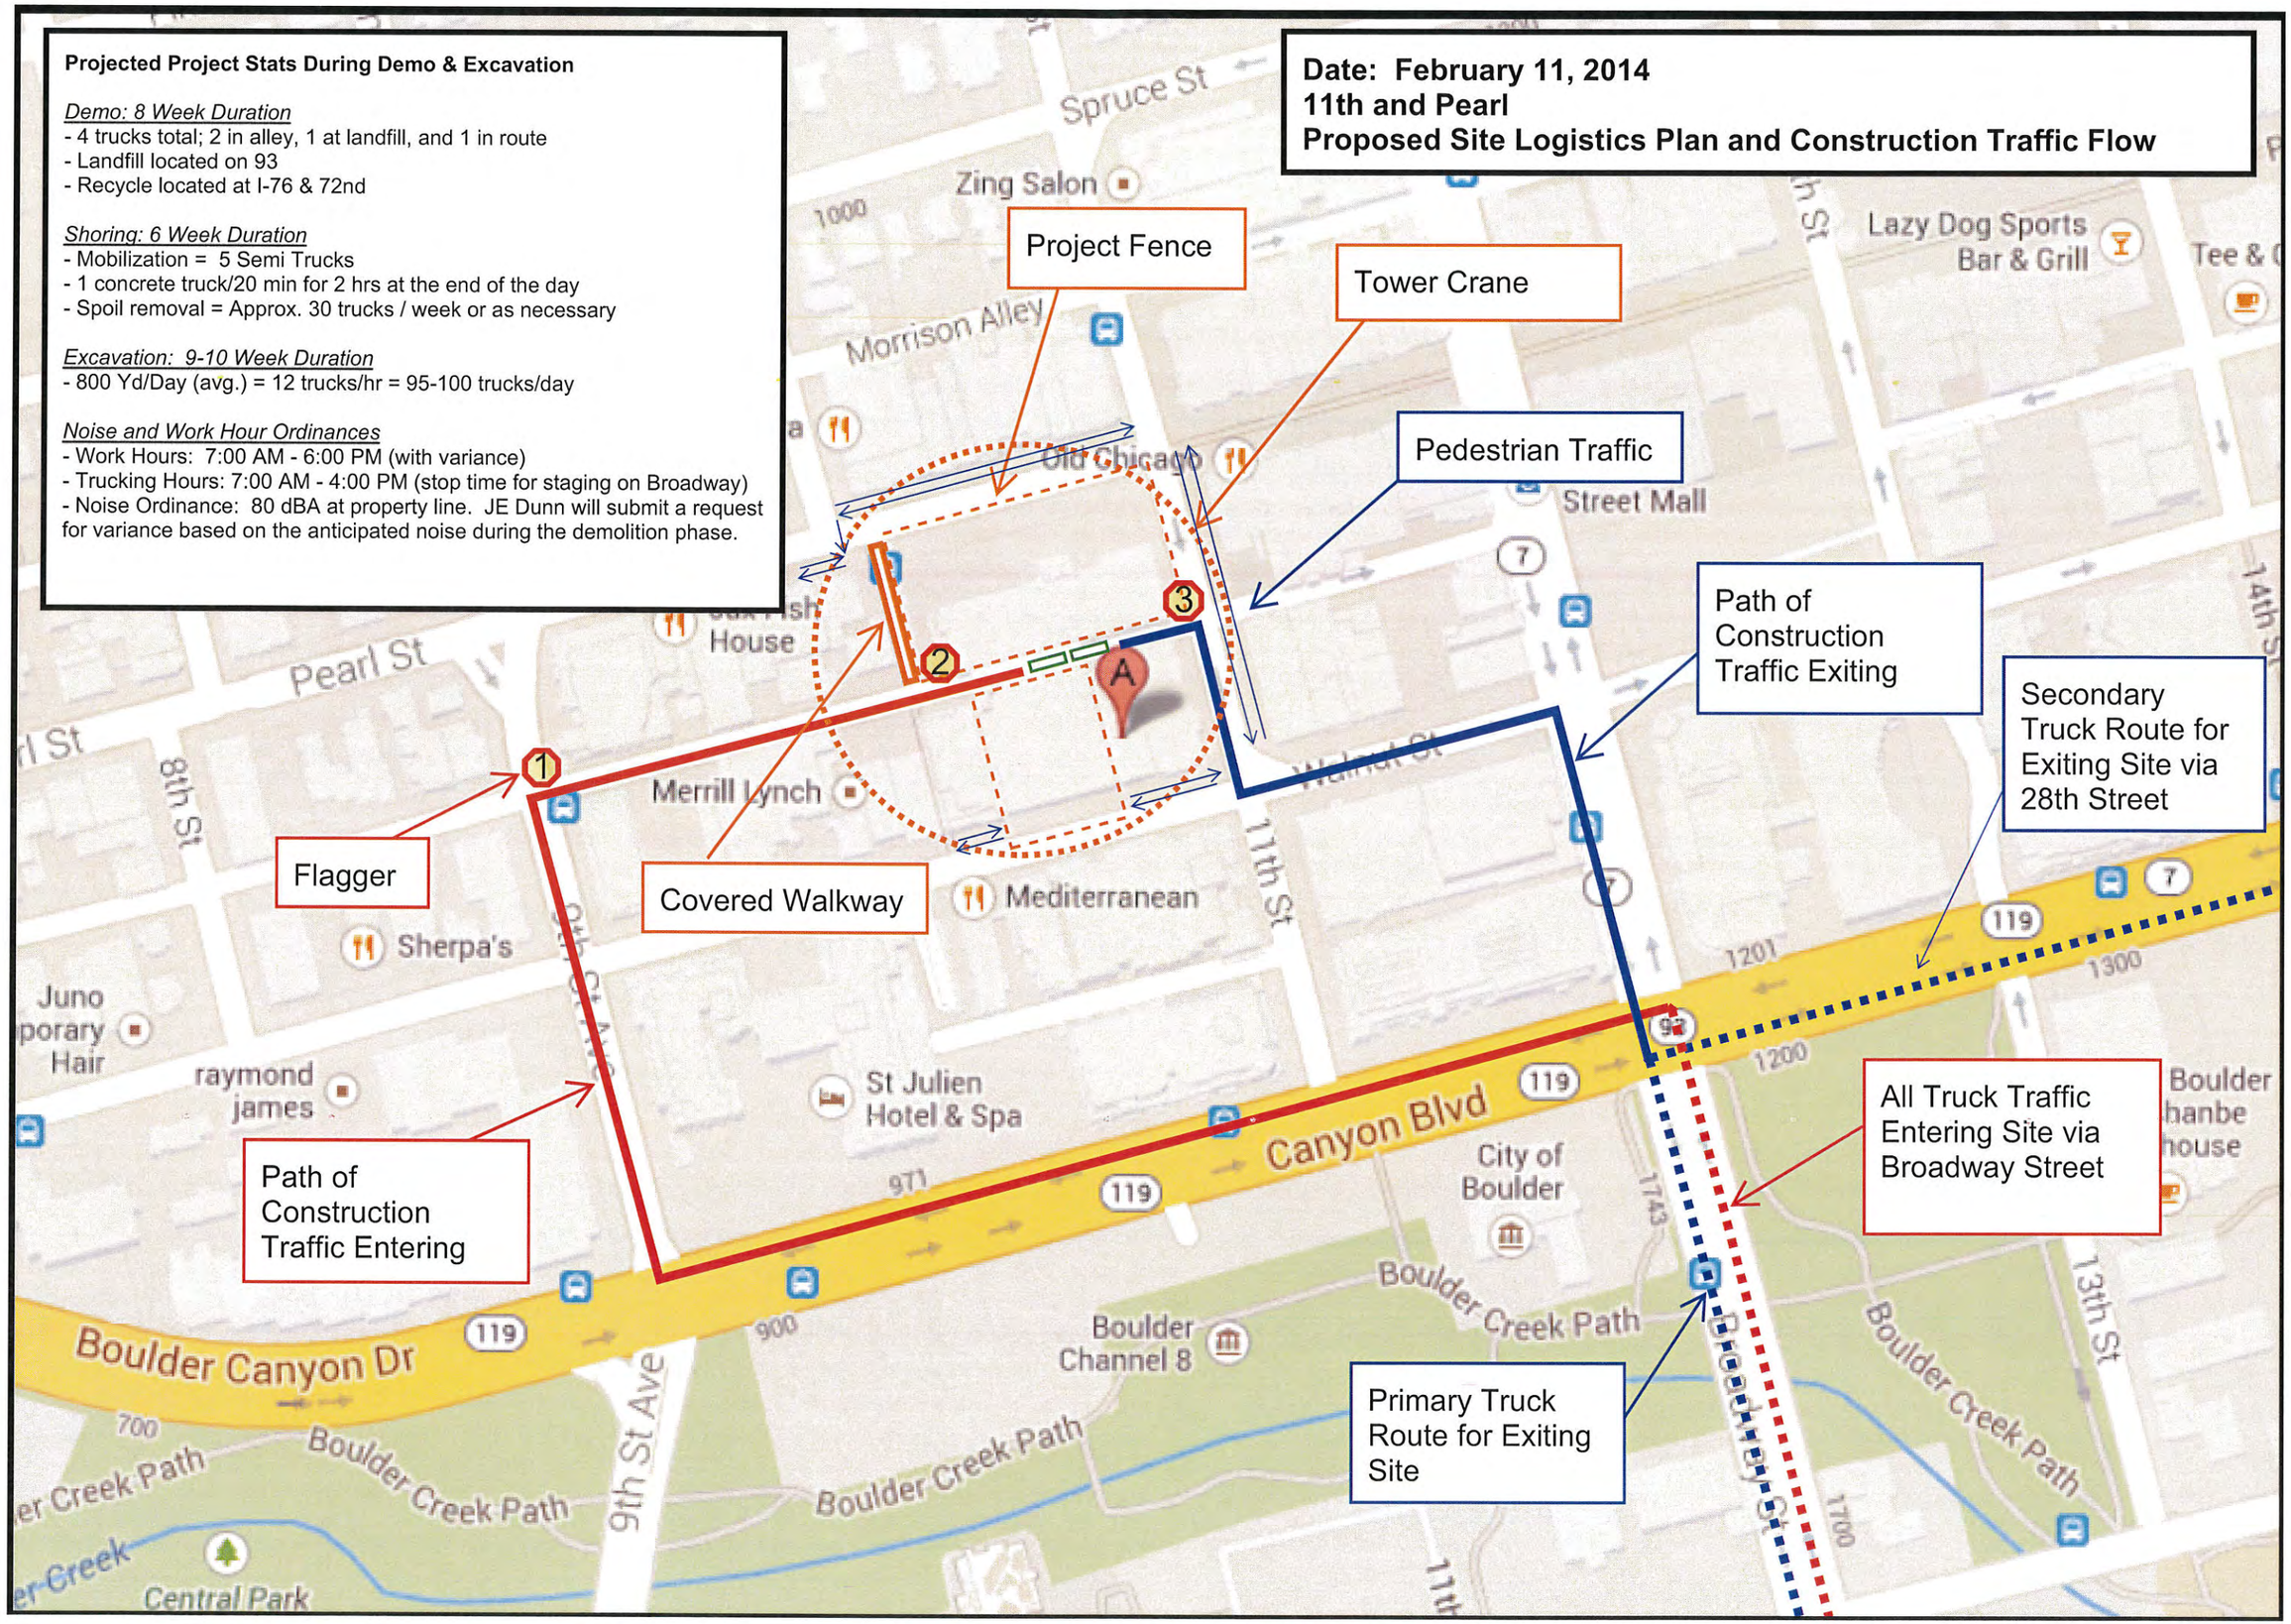
Date: February 11, 2014
11th and Pearl
Proposed Site Logistics Plan and Construction Traffic Flow
